

# PROJECT MANAGEMENT

(593)

—Post-secondary—

—OPEN EVENT—

**NATIONAL – 2019**

DO NOT WRITE ON TEST BOOKLET

*TOTAL POINTS*

\_\_\_\_\_ (100 points)

Failure to adhere to any of the following rules will result in disqualification:


1. Contestant must hand in this test booklet and all printouts. Failure to do so will result in disqualification.
2. No equipment, supplies, or materials other than those specified for this event are allowed in the testing area. No previous BPA tests and/or sample tests or facsimile (handwritten, photocopied, or keyed) are allowed in the testing area.
3. Electronic devices will be monitored according to ACT standards.

No more than sixty (60) minutes testing time

Property of Business Professionals of America.  
May be reproduced only for use in the Business Professionals of America  
*Workplace Skills Assessment Program* competition.

Identify the letter of the choice that best completes the statement or answers the question.

- 1) Each of 10 project phases has a 99% chance of completion on time. What is the probability that all 10 project phases will be completed on time?
  - a) 99%
  - b) 95%
  - c) 90%
  - d) 100%
- 2) The project manager suggests a smartphone app be created for all stakeholders to post key measures. This is an example of
  - a) Stakeholder mitigation
  - b) Work performance data
  - c) Managing communications
  - d) Developing stakeholders

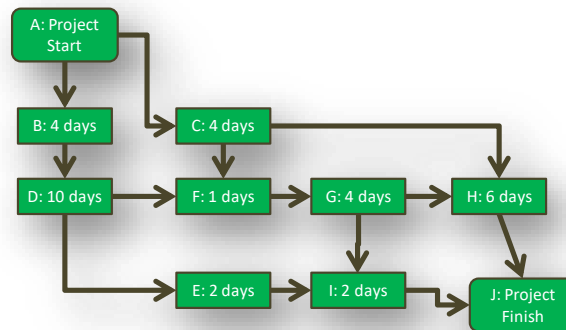

- 3) Based on the above precedence diagram, if process C is increased to 8 days, what is the critical path?
  - a) ACHJ
  - b) ABDFGIJ
  - c) ABDEIJ
  - d) ABDFGHJ
- 4) Based on the above precedence diagram, if step C is reduced to 3 days, what is the new critical path?
  - a) ACHJ
  - b) ABDFGIJ
  - c) ABDFGHJ
  - d) ABDEIJ
- 5) A project charter establishes a partnership between what two organizations?
  - a) Planning and Executing
  - b) Performing and Requesting
  - c) Management and Sponsors
  - d) Performing and Monitoring

- 6) Calculate the expected value using the following three-point estimates: Optimistic (O) = 6, Most likely (M) = 8, and Pessimistic (P) = 10.
- a) 6
  - b) 8
  - c) 12
  - d) 11.5
- 7) If a project manager has a project with an SPI of 1.05, what should they do immediately?
- a) Call a meeting to revise the project budget.
  - b) Look for alternatives and create change notices.
  - c) Do nothing. All is well.
  - d) Stop the project.
- 8) Breakdowns in communication will \_\_\_\_\_ impact the project.
- a) usually positively
  - b) usually negatively
  - c) always positively
  - d) always negatively
- 9) A requirements traceability matrix can be used to control \_\_\_\_\_.
- a) the project charter
  - b) the stakeholders
  - c) key project deliverables
  - d) the project schedule
- 10) \_\_\_\_\_ is an input into the direct and manage project work process
- a) Project management plan
  - b) Deliverables
  - c) Expert judgment
  - d) Meetings
- 11) There are \_\_\_\_\_ process groups, \_\_\_\_\_ knowledge areas and \_\_\_\_\_ processes in project management.
- a) 10, 14, 47
  - b) 5, 14, 57
  - c) 5, 10, 47
  - d) 10, 14, 57
- 12) During a conference call with team members, someone is typing in the background. The typing is an example of \_\_\_\_\_ in the communication model.
- a) Interference
  - b) Noise
  - c) Annoyance
  - d) Encoding

- 13) If you are working with a team that has experience working together on past projects, what is the *best* way to get a quick estimate on the overall project cost?
- a) Three-point estimating
  - b) Legitimate power
  - c) Analogous estimating
  - d) Rolling wave estimating
- 14) As a project manager, you notice that there is a promotion that a key team member has applied for. This is a risk \_\_\_\_\_.
- a) Occurrence
  - b) Trigger
  - c) Discovery
  - d) Process
- 15) Your project has a cost performance index of 1.2 and a schedule performance index of 0.85. The project is
- a) costs below budget and is ahead of schedule
  - b) costs below budget and is behind schedule
  - c) costs over budget and is ahead of schedule
  - d) costs over budget and is behind schedule
- 16) Your project has a budget at completion of \$5,000,000. The earned value is \$4,500,000 and actual cost is \$4,800,000. What is the remaining budget?
- a) \$500,000
  - b) \$200,000
  - c) \$4,500,000
  - d) \$4,800,000
- 17) Your virtual project team has developed some bad habits during meetings. What should a project manager do to reduce or prevent such problems?
- a) Bring in a trainer to work on soft skills such as empathy or compassion
  - b) Conduct a face to face meeting to discuss behavior expectations
  - c) Have the project team agree upon clear expectations and rules for meetings
  - d) Organize a team building event
- 18) You have assumed the responsibility for an existing project. You notice that Chris would be a critical resource because of his engineering knowledge. As part of the resource planning process, you \_\_\_\_\_ Chris' boss to allocate his time for the project.
- a) require
  - b) compromise with
  - c) change notify
  - d) negotiate with

- 19) Crashing and fast tracking a project are examples of \_\_\_\_\_.  
a) Schedule compression  
b) Motivation  
c) Resource smoothing  
d) Resource leveling
- 20) At a progress meeting, the team informs you that several areas of quality are below project expectations. As a project manager, what should you do next?  
a) Call a meeting with key stakeholders  
b) Stop the project  
c) Develop a statistical analysis  
d) Discipline the team
- 21) A multi-variable analysis that helps to understand which variables have the most influence on a process is called a \_\_\_\_\_.  
a) Process map  
b) Prototype  
c) Design of experiment  
d) Scatter diagram
- 22) The most important output from the plan human resource management process is the  
a) change log  
b) enterprise organizational assets  
c) organizational breakdown structure  
d) documentation of the project manager's authority
- 23) Smoothing is a type of conflict resolution that \_\_\_\_\_.  
a) the project manager retreats from the conflict  
b) keeps the atmosphere friendly, does not resolve conflict, only delays it  
c) one person's viewpoint is exerted at the expense of another person  
d) involves therapy and consultants to come to a common understanding
- 24) When workers in a project need to be constantly watched and directed, this is an example of \_\_\_\_\_.  
a) Herzberg's theory of motivation  
b) Maslow's hierarchy of needs theory  
c) McGregor's Theory Y  
d) McGregor's Theory X
- 25) About 55% of all communication which is commonly known as body language is \_\_\_\_\_.  
a) Para lingual communication  
b) Active listening  
c) Effective listening  
d) Nonverbal communication

- 26) As the project manager on a project nearing end with 75% of your workers being offsite contractors, your company decides to implement new technology for internal communications. Should you implement this technology for your project team's use?
- a) Yes, it may give your team an advantage.
  - b) Yes, because the current system is obsolete.
  - c) No, it may add cost to the project.
  - d) No, since timing and location prohibit a cost benefit.
- 27) The results of a \_\_\_\_\_ provide a cumulative probability distribution for achieving a value of cost or time
- a) Rolling wave analysis
  - b) Monte Carlo simulation
  - c) FMEA
  - d) Defect concentration diagram
- 28) When a project manager has a project with multiple phases, it is probable that risks will
- a) be the same in each phase
  - b) be resolved at the end of each phase
  - c) be completely different in each phase
  - d) be resolved before starting each phase
- 29) All of these are procurement contract types *except*
- a) Fixed price
  - b) Time and material
  - c) Cost reimbursable
  - d) Intent
- 30) You are a project manager on a new project. Many of the stakeholders identified in the charter are high-ranking executives in the current organization. One method for developing a strategy to manage stakeholders is
- a) Complete the stakeholder register
  - b) Conduct interviews with all stakeholders
  - c) Negotiate with the stakeholders for resources
  - d) Perform a power/interest analysis
- 31) The project you are currently managing is behind schedule and over budget. You determine that the Planned value is \$350,000, Actual cost is \$378,000, and Earned value is \$346,000. What management reserve should you ask for to get your project back to a CPI and SPI of 1.0?
- a) \$50,000
  - b) \$28,000
  - c) \$32,000
  - d) \$5,000

- 32) A \_\_\_\_\_ establishes a partnership between the performing and requesting organizations in a project?
- a) handshake
  - b) project charter
  - c) memo
  - d) verbal notice
- 33) A milestone is a \_\_\_\_\_ and an activity has \_\_\_\_\_.
- a) Point in time, duration
  - b) Project goal, purpose
  - c) They are the same thing
  - d) Stopping point, duration
- 34) Risks that can be identified and analyzed are called \_\_\_\_\_.
- a) Risk responses
  - b) Risk estimates
  - c) Known risks
  - d) Reported risks
- 35) What four-step cycle to improve project quality is W. Edwards Deming well known for?
- a) DMAC
  - b) PDCA
  - c) PDAC
  - d) FMEA
- 36) If activity durations are estimated before assigning team members, what is a potential problem?
- a) Team member competency may affect activity durations.
  - b) Activity durations will be unchanged by this.
  - c) Project scope may be affected.
  - d) Quality assurance activities may need to be changed as a result.
- 37) If a project manager has a project with an SPI of 0.41, what should they do immediately?
- a) Realize the project is ahead of schedule.
  - b) Realize the project is behind schedule..
  - c) Do nothing. All is well.
  - d) Stop the project.
- 38) Performance reporting is the process of \_\_\_\_\_.
- a) collecting procurements, issuing supplier invoices and documenting reports..
  - b) collecting and distributing status, progress and forecast reports..
  - c) information change logs
  - d) performance reporting to stakeholders

- 39) \_\_\_\_\_ can be used to control key project deliverables.
- a) The project charter
  - b) The stakeholders analysis
  - c) A requirements traceability matrix
  - d) The project schedule
- 40) Matrix organizations reflect \_\_\_\_\_.
- a) A functional organization on a spreadsheet
  - b) A blend of a functional and project focused characteristics.
  - c) A single authority to make all project decisions
  - d) Each employee having one clear superior
- 41) Which type of change request can have implications for the project management plans, policies, procedures, schedules, costs, and budgets?
- a) Rejected
  - b) Deferred
  - c) Declined
  - d) Approved
- 42) What is the PDCA or Shewhart cycle stand for?
- a) Plan Do Change Accept
  - b) Plan Do Change Act
  - c) Plan Do Check Act
  - d) Plan Do Check Accept
- 43) There are two Earned Value Management variance formulas that calculate Schedule Variance and Cost Variance. They include all of these values *except* \_\_\_\_\_.
- a) Earned Value
  - b) Actual Cost
  - c) Planned Value
  - d) Cost Performance Index
- 44) These are all *valid* reasons for chartering a project *except* \_\_\_\_\_.
- a) Social need
  - b) Legal requirement
  - c) Market analysis
  - d) New technology development
- 45) The quality management plan will need to define appropriate levels of quality, grade, \_\_\_\_\_.
- a) precision and accuracy
  - b) cost and expense
  - c) liability and risk
  - d) schedule and cost



- 46) Distribution of a procurement document package to selected sellers will result in getting what in return?
- a) Proposals
  - b) Invoices
  - c) Quotations
  - d) Requirements
- 47) Several authors provide different estimates for your projects' training and operation manuals. If the range of estimates is too great, what should you do?
- a) Select the seller with the lowest estimate.
  - b) Force ranking the sellers on each criterion.
  - c) Perform your own independent estimate.
  - d) Pick the most familiar seller.
- 48) You realized that you have *not* been fair to one of your project team members. What would be the appropriate course of action?
- a) Apologize to the other team members.
  - b) Remind yourself to be fair next time.
  - c) Do not do anything, it is in the past.
  - d) Take corrective actions as appropriate.
- 49) In the utility theory of risk tolerance, \_\_\_\_\_ is a type of preference to consider for stakeholder risk?
- a) Risk norming
  - b) Risk forming
  - c) Risk storming
  - d) Risk seeking
- 50) You serve on a board of directors of a local organization. The local organization was voting on a motion that could potentially benefit your employer but not you personally. As part of your duty as a project management practitioner, you should \_\_\_\_\_.
- a) support the motion and suggest hiring your employer
  - b) abstain from the discussions to avoid the perception of conflict of interest
  - c) point out all deficiencies of all potential proposals
  - d) assess all options and then offer your impartial and expert opinion to the group
